

Sterling Highway MP 45 to 60



Roads and Highways Advisory Board
November 5th, 2024






Project Phasing





New Construction Schedule

2024 Cost, Schedule, and Risk Assessment (CSRA) \$894,000,000 Total Cost to Complete (YOE)

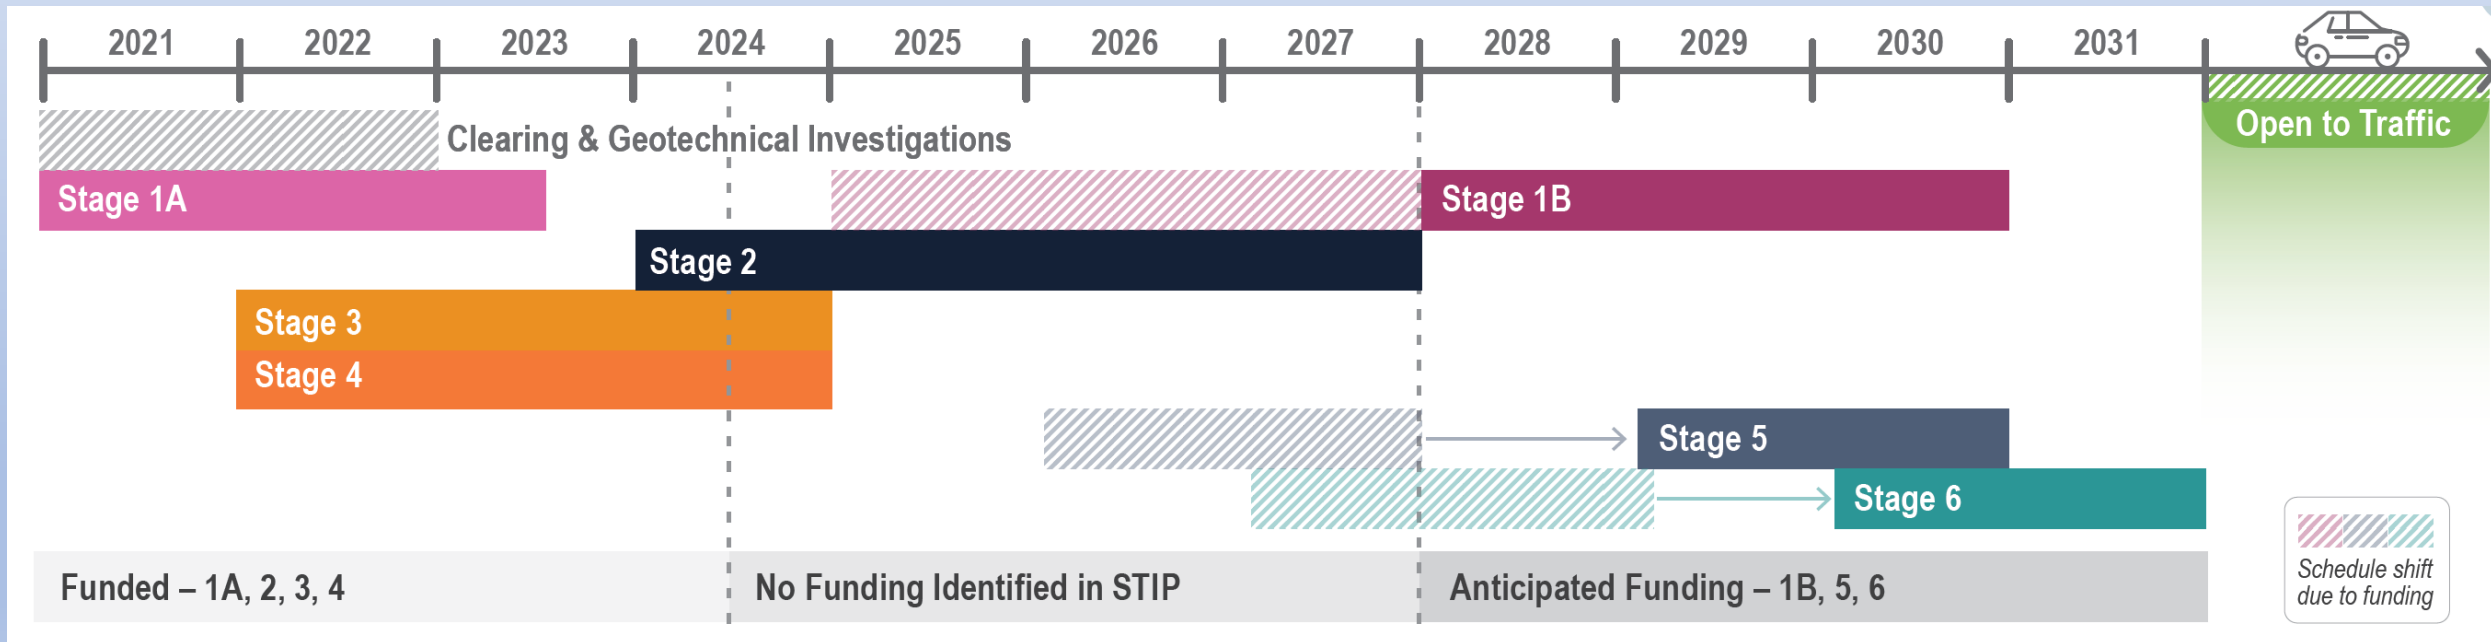



Construction Funding to Date

| Contractor | Stage | Award Amount | Remaining Balance |
|----------------|-----------------------------|---------------|-------------------|
| Kiewit | Advanced Clearing | \$2,929,580 | \$0 |
| Scarsella Bros | Stage 1A (MP56-58) | \$20,130,326 | \$0 |
| QAP | Pioneer Roads | \$4,500,000 | \$0 |
| QAP | Stage 3 & 4 Early Earthwork | \$104,692,858 | \$14,809,233 |
| Traylor | Stage 2 Juneau Creek Bridge | \$151,327,688 | \$95,177,688 |



Phase 2 Bridge

2024





Phase 3

East Side of
Bridge



Phase 4
Looking
towards FS
Ramps

2023



Phase 5

2023





2023 Archeological Program:

- 25-30 Archeologist's
- Surveyed over 40 Acres (Over 300 total)
 - Documented 14 new sites
 - Re-Documented 15 existing sites
- Moved the equivalent of 40 tons material

Overall

- 4 Acres of Cultural Sites affected
- Archeological Program will take 7-8 years to complete
- Estimated cost of about \$50million





2024

Wildlife Crossing





Future Funding Strategies

1. **Innovative Financing** – The Department will continue to prepare grants for specific stages of the project. We have applied for multiple grants to date with no success, will continue to pursue opportunities.
2. **Develop Stages to Final Design:** This will allow the project stages to take advantage of any funding that may become available through other projects slipping or other projects being able to take advantage of grants.
